


MEASURE M PROJECT UPDATE

March 10, 2020



MARIE BAUER



- Project bid September 19, 2019
- Project awarded October 8, 2019
- \$10,513,428 (Construction costs only)
 - Estimate the actual cost will be close to \$12,800,000 (including architect fees, soft costs, etc.)
- Slab is poured and framing is started on Building A. Building B pad is complete, and footings and utilities are underway.
- Expected completion is October 2020




GLEN SPECK



- Project bid September 19, 2019
- Project awarded January 25, 2020
- \$19,092,000
- Demolition work is almost completed
- Draft schedule will be provided by the contractor shortly
- Anticipated completion is Aug 2021



GLEN SPECK

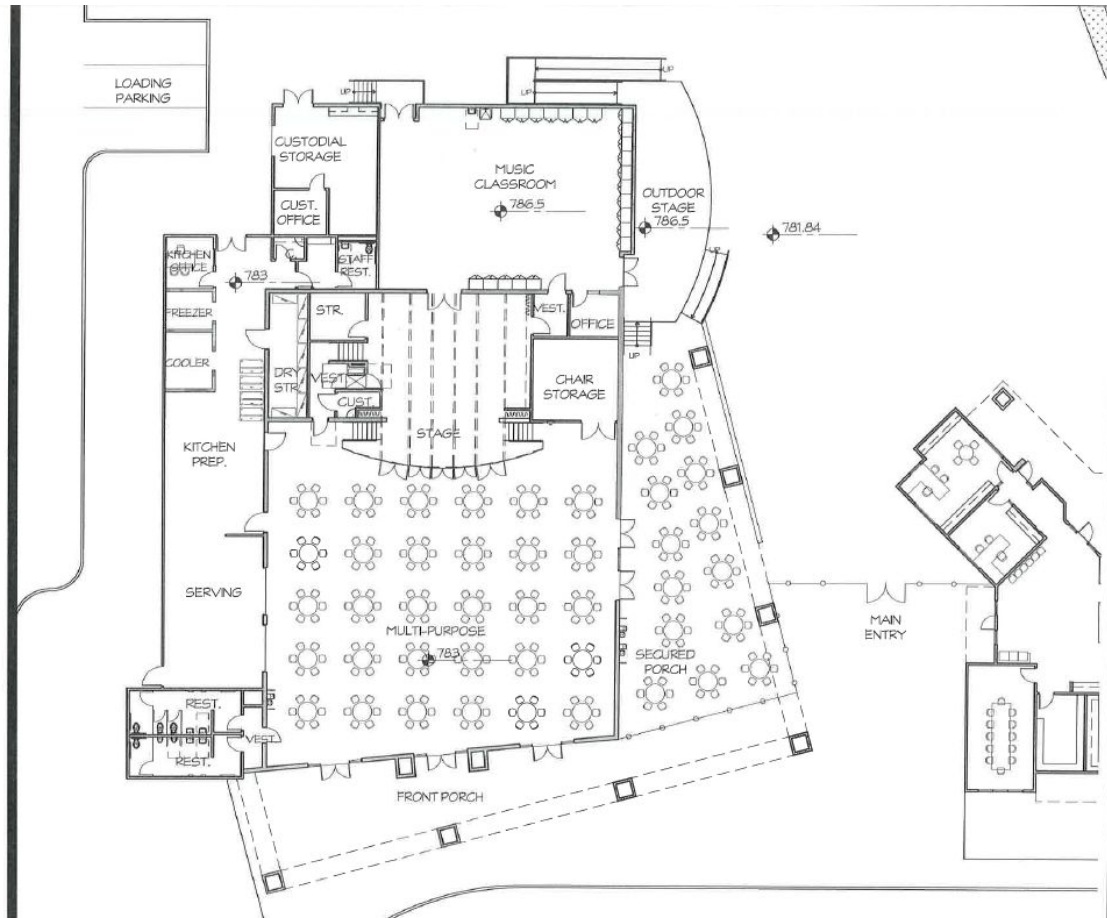


GLEN SPECK ACADEMY OF ARTS



PASO ROBLES

JOINT UNIFIED SCHOOL DISTRICT
THE DISTRICT OF EXCELLENCE

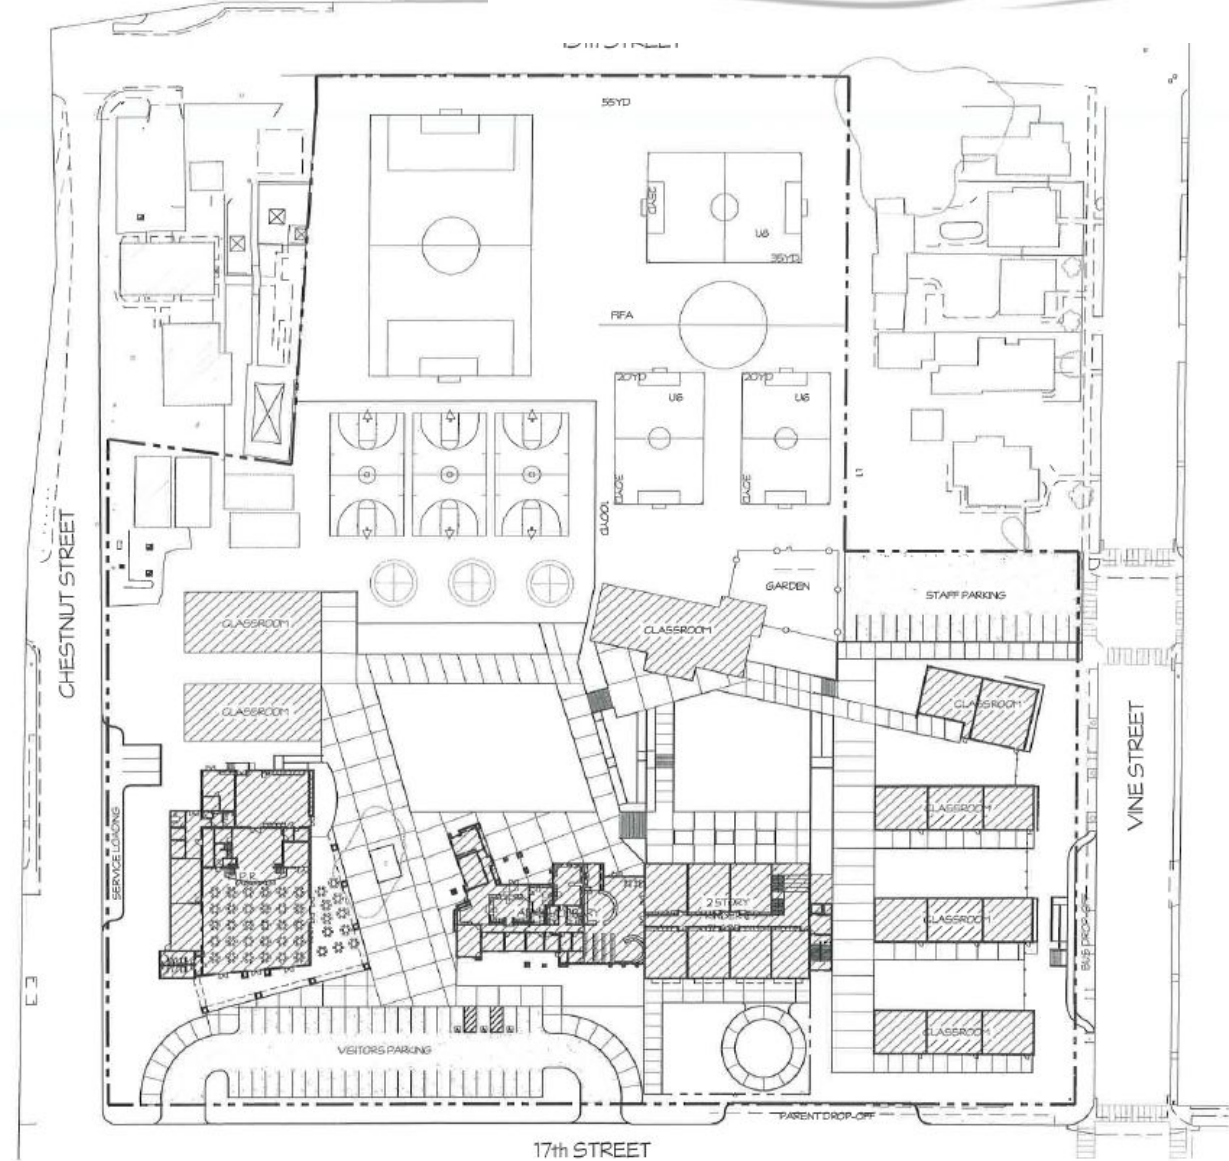

SITE PLAN
XXXXXX



FLAMSON CLASSROOM



- Project bid January 8, 2019
- Project awarded January 22, 2019
- \$5,297,000 (Construction costs only)
 - Estimate the actual cost will be close to \$6,500,000 (including architect fees, soft costs, etc.)
- Project is at 80% completion. Interior finish work is in progress. Exterior plastering is underway.
- Substantial completion date is currently 4/24/20




TAABS TEMPORARY CAMPUS



- Project bid January 8, 2019
- Project awarded January 22, 2019
- \$5,297,000 (Construction costs only)
- Portable restroom is set
- Shade structure delivery is 4 weeks out
- Gate in the alley is in place.
- Electronic opener is planned to be operational after 3/20/20



GEORGIA BROWN

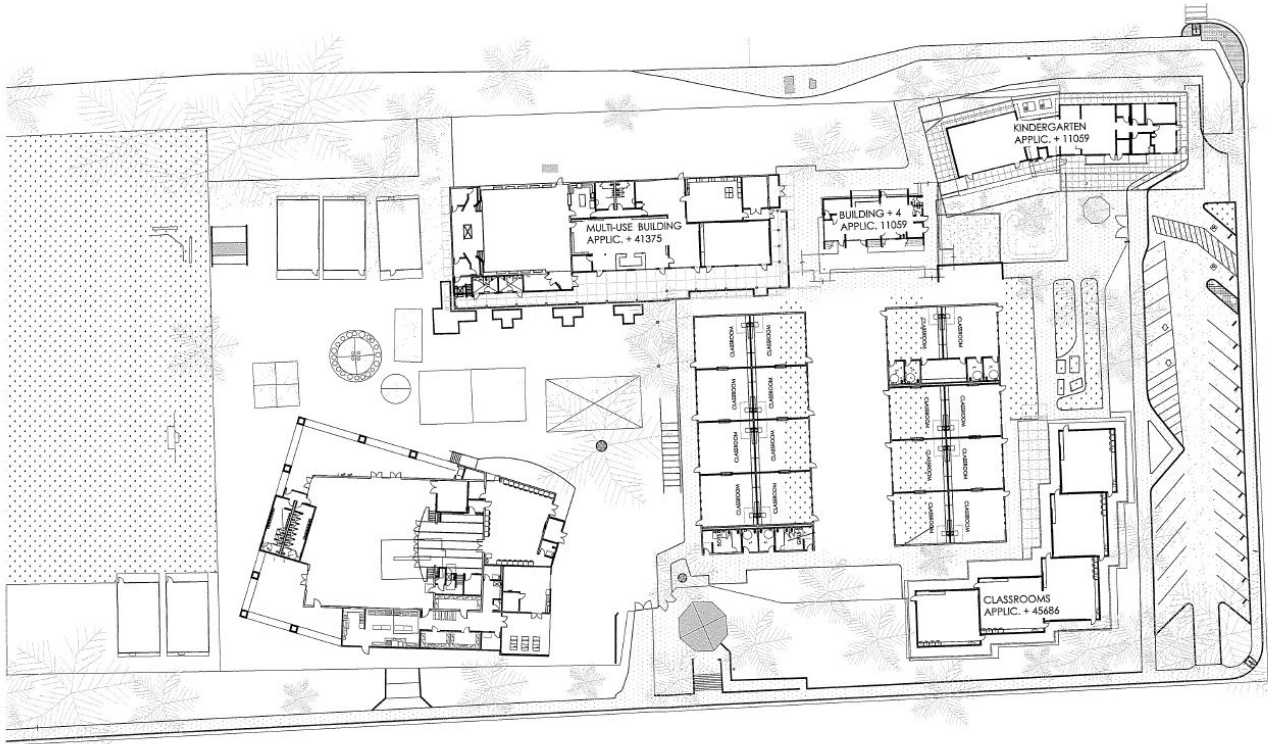

- Staff has conducted multiple planning charrettes
- Early conceptual plan
- Decision should be made by Mid-May on full plan of construction to stay on schedule



SUMMARY AND QUESTIONS

- Monthly updates will continue
- Discussion regarding the next bond sale upcoming
- Update of Measure M budget
- March 24, 2020 - Discussion regarding workforce house by Dale Scott
- Questions?

