

Bond Project Office Update
Board of Trustees Meeting,
September 10, 2020

Measure BB-2018


Peterson Middle School Locker Building and Pool Replacement



- Interior framing and utility rough-in are in progress.
- Completion is still on track for spring 2021.

Elementary School Exterior Improvements Program

- This chart shows the schools under construction this summer (yellow). The shade structure at Washington Open will be completed next summer because of required geotechnical surveys, reports and approvals.

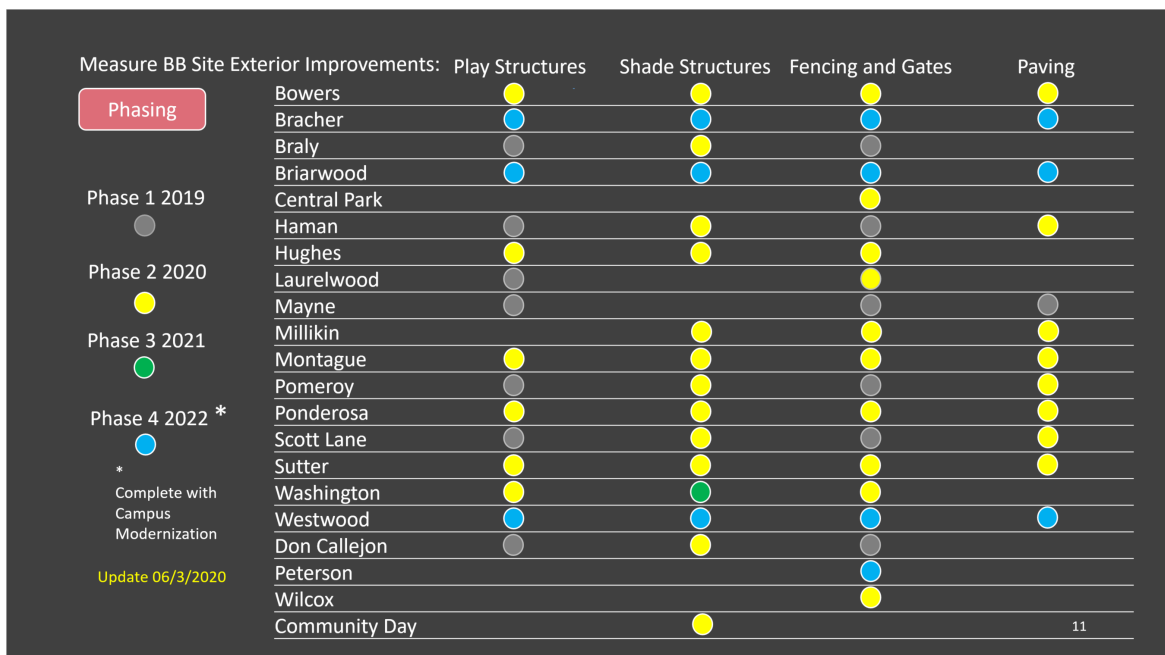

Elementary School Exterior Improvements Program [continued]

- COVID-19 has interrupted manufacturing of equipment and shade structures.
- Work will continue on most sites into the school year.
- Shade structures are now under construction and will be completed by October.
- Staff as completed temporary fencing and barricades to facilitate staff access to the campuses while work is underway. Many play structures are complete.
- Extensive site construction and added asphalt paving are extending work a some sites.



Shade Structure Column Footing Reinforcing, Haman E.S.



Bowers E.S.



Ponderosa E.S.

Santa Clara and Wilcox High School Synthetic Turf Fields

- The stadium fields are substantially complete.
- The practice fields are scheduled to be complete in October.



Wilson Education Options Campus

- The roofing project is complete
- Landscaping and drainage improvements are 80% complete.



Patrick Henry, Laurelwood, Peterson Program

- The second phase of fencing and paving improvements are nearing completion at Laurelwood Elementary School.
- Staff has developed a proposed plan to replace the Peterson fields.
- Staff is working on procuring consultants for the new school in preparation for outreach in the fall.

Elementary School Metal Roofing Program

- Plans for the following schools are being reviewed by DSA:
 - Hughes Elementary: Multipurpose Building
 - George Mayne Elementary: Six buildings
 - Scott Lane Elementary: Five buildings
 - Washington Open Elementary: Two buildings

New High School at Agnews

- Contracts have been awarded for Groups 1 and 2 bid packages.
- Foundation construction has begun.
- Contract awards to-date are within the project budget.

Measure H-2014

Abram Agnew Elementary School

Dolores Huerta Middle School

- Exterior plaster and interior gypsum board are underway.
- Staff is continuing to assess cost and schedule issues.
- The schools are on track to open next August.

Zanker Road Improvements

- The Traffic Impact fee in the amount of \$4,866,432.00 has been paid. The payment was submitted with a letter of protest.
- Construction has begun.

Buchser Middle School Tennis Courts and PE Improvements

- The project is substantially complete. The fence screen is being completed.
- Punchlist inspections are underway.
