

**Santa Rosa High School District
2014 General Obligation Bond Authorization
Measure I
Citizens' Oversight Committee**

Annual Report

JULY 2019

January 31, 2018 – December 31, 2018



Santa Rosa City Schools

Tel (707) 890-3800

211 Ridgway Avenue
Santa Rosa, CA 95401

<http://www.srscschools.org>

Table of Contents

Contents

Bond Background _____	1
Activities _____	4
Bond Financials _____	5
Fiscal and Performance Audit _____	11
Photos _____	12
Committee Members _____	20
Contact Information _____	21

“Thank you Santa Rosa community for your support in preparing our students for college and careers.

Measures I and L will serve to upgrade facilities, address overcrowding, and infuse classroom technology and associated access, in order to better serve our students.” – Diann Kitamura , Superintendent, Santa Rosa City Schools

Bond Background

Measure I

On November 4, 2014, the voters of the Santa Rosa High School District authorized measure I under the Proposition 39 statutes. Measure I authorized the issuance of \$175 million in General Obligation Bonds. Proceeds from the sales of the Bonds will be used to finance the acquisition, construction, furnishing, and equipping of District facilities in accordance with the bond proposition approved at the Election, and a project list including basic school repairs, upgrades and capital improvements to classrooms, labs and facilities, school safety, and technology improvements to provide a 21st Century Education.

Ballot Question: “To improve high school educational quality and student safety by upgrading classrooms and science labs, replacing deteriorating and outdated plumbing, heating, ventilation and air-conditioning systems, providing updated 21st century classroom technology, and acquiring, renovating or constructing classrooms, equipment, sites and facilities, shall Santa Rosa High School District issue \$175 million in bonds at legal rates, including independent citizens’ oversight, annual audits, no money for administrators’ salaries* and all funds benefiting local schools (State cannot take the funds).”

*The prohibition does not include employees who oversee and administer the bond program.

What will Measure I do?

Measure I will improve our local middle and high schools by:

- Providing up-to-date, 21st-century technology to prepare students for college and careers
- Repairing leaky roofs and deteriorating plumbing, sewer and electrical systems
- Replacing outdated heating and air conditioning systems
- Improving access to classrooms and labs for students with disabilities
- Upgrading campus security, safety and fire systems at all schools
- Renovating aging classrooms, science, labs, restrooms and other educational facilities

Citizen's Oversight Committee (COC)

In accordance with bond spending rules, Santa Rosa City Schools has convened a Citizen's Bond Oversight Committee to keep the public informed. This committee will review Measure I bond expenditures, review the annual audit prepared by an independent auditing firm, and ensure that funds are spent according to the terms of the ballot language.

District will solicit applications from the community to form the oversight committee. By law, the oversight committee must include a member active in business organization, a member active in a senior citizens' organization, a member active in bona fide taxpayers' organization, a member active in the Parent Teachers Association (PTA) as well as a member who is a parent or guardian of a child enrolled in the District. No employee or official of the District can be appointed to the oversight committee.

Role of the Citizens' Oversight Committee:

- Ensure bond revenues are expended only for construction, reconstruction, rehabilitation, or replacement of school facilities.
- Inform the public concerning expenditure of bond proceeds
- Review annual performance audit
- Review annual financial audit
- Inspection of school facilities & grounds to ensure expenditures are for listed projects
- Review District efforts to maximize bond revenues through implementation of cost containment measures:
 - Professional fees
 - Site preparation
 - Joint use of facilities
 - Design deficiencies
 - Reusable facilities plans
- Provide an annual progress report to the Board and the public
- Provide final report to the Board and the public at the completion of all projects
- Review deferred maintenance reports and plans

Facility Master Plan (FMP)

The Santa Rosa City Schools Facility Master Plan (FMP) was developed to identify and prioritize projects for each of the High Schools. The FMP was approved by the Santa Rosa City School Board of Education on April 27, 2016.

Role of the Board of Education

- For a Prop. 39 Bond:
 - Places bond measure on ballot
 - Appoints COC
 - Establishes guidelines for the COC
 - Approves bond program project list and an implementation plan
- Evaluate school facilities needs
- Approve additions or alterations to existing buildings
- Determine when new facilities are needed
- Select and acquires sites
- Determine the method of financing
- Approve selection of architects and engineers
- Authorize projects for bid
- Award contracts for design and construction
- Approve change orders to construction contracts

Activities

Citizens' Oversight Committee (COC)

January 18, 2018	General Bond Program Status.
April 19, 2018	General Bond Program Status; Carrillo Field Visit; Annual Report review.
July 25, 2018	Presentation to School Board.
August 23, 2018	General Bond Program Status.
December 19, 2018	General Bond Program Status.

Bond Financials

Measure I General Obligation Bond Sales

Total Bond Authorization	\$ 175,000,000
Series A sold February 2016	\$ 12,165,000
Series B sold December 2016	\$ 50,000,000
Series C and D Sold June 2018	\$ 70,000,000

Santa Rosa City School
Measure I - Secondary Bond Program
Program Snapshot through 01/01/18-12/31/18

Measure I Voter Authorization	\$	175,000,000
Measure I Series A, B, C, D Issuances	\$	132,165,000
Remaining Bond Authorization	\$	42,835,000
Interest	\$	1,188,771
Cost of Issuances, Debt Service, COI Refund	\$	(613,737)
Election Costs	\$	(45,037)
Net Proceeds from Series A & B (Cash on Hand Before Expenditures)	\$	132,694,997

Expenditure Overview	Expenditures 2016	Expenditures 2017	Expenditures 2018	
Facilities Projects - Construction	\$ 496,577.23	\$ 6,918,965.81	\$ 23,229,298.42	\$ 30,644,841.46
Design/Engineering/Inspection Services	\$ 2,190,774.44	\$ 1,116,760.25	\$ 4,404,692.32	\$ 7,712,227.01
Technology Projects Cost	\$ 11,333,156.23	\$ 4,407,745.37	\$ 4,143,791.55	\$ 19,884,693.15
Bond Administration	\$ 146,463.22	\$ 420,592.14	\$ 534,076.00	\$ 1,101,131.36

Program Budget Totals	Budget**	Disbursement 2016	Disbursement 2017	Disbursement 2018	Budget Remaining As of 12/31/2017 (Budget - Encumbered=Total)
Facilities Program Budget	\$ 145,341,246	\$ 2,833,814.89	\$ 8,456,318.20	\$ 28,168,066.74	\$ 105,883,046.17
Technology Program Budget	\$ 29,000,000	\$ 11,333,156.23	\$ 4,407,745.37	\$ 4,143,791.55	\$ 9,115,306.85
Bond Program Totals	\$ 174,341,246	\$ 14,166,971.12	\$ 12,864,063.57	\$ 32,311,858.29	\$ 114,998,353.02

**Budget indicates amount based on total Measure I Authorization (\$175,000,000) less Election and Issuance Costs

2018 Program Summary - Measure I

January 1, 2018 - December 31, 2018

PROJECT	BUD TOTAL	ENCUMBERED	DISBURSEMENT	BUD REMAIN.	ENC BALANCE
000-0000-0000 - District Wide	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
200-0000-0000 - Secondary Schools	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
230-9806-5192 - Cook Middle - Portable Classrooms	\$0.00	(\$0.85)	(\$39,257.60)	\$0.85	(\$39,258.45)
230-9851-5192 - Cook Middle - Site Improvements	\$0.00	(\$2,431.09)	\$0.00	\$2,431.09	(\$2,431.09)
231-9540-5192 - Slater Middle - Asbestos/Hazardous Materials	\$2,636.00	\$0.00	\$0.00	\$2,636.00	\$0.00
231-9566-5192 - Slater Middle - School Signage	\$14,500.00	\$27,976.04	(\$27,976.04)	(\$13,476.04)	\$0.00
231-9650-5192 - Slater Middle - Other Fees	\$0.00	\$78,750.00	(\$78,750.00)	(\$78,750.00)	\$0.00
231-9821-5192 - Slater Middle - Roofing Replacement	\$0.00	(\$46,216.00)	(\$44,765.65)	\$46,216.00	(\$90,981.65)
232-9540-5192 - Comstock Middle - Asbestos/Haz. Mat.	\$0.00	\$1,038.00	(\$1,038.00)	(\$1,038.00)	\$0.00
232-9806-5192 - Comstock Middle - Portable Classrooms	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
232-9821-5192 - Comstock Middle - Roofing Replacement	\$0.00	\$6,197,666.76	(\$4,389,791.20)	(\$6,197,666.76)	\$1,807,875.56
232-9851-5192 - Comstock Middle - Site Improvements	\$0.00	\$463.16	(\$463.16)	(\$463.16)	\$0.00
234-9851-5192 - Santa Rosa Middle - Site Improvements	\$61,050.00	\$61,050.00	\$0.00	\$0.00	\$61,050.00
243-9816-5189 - Lewis / Alternative Ed - Hvac Systems	\$22,987.00	\$22,987.00	\$0.00	\$0.00	\$22,987.00
249-9403-5192 - Secondary District Wide - Security	\$0.00	(\$17,500.00)	\$0.00	\$17,500.00	(\$17,500.00)
249-9500-5192 - Secondary District Wide - Athletic Fields	\$443.21	\$0.00	\$0.00	\$443.21	\$0.00
249-9531-5192 - Secondary District Wide - Site Safety	\$0.00	\$6,594.80	(\$7,875.00)	(\$6,594.80)	(\$1,280.20)
249-9650-5192 - Secondary District Wide - Other Fees	\$2,891,892.95	\$5,844,965.00	(\$3,444,375.17)	(\$2,953,072.05)	\$2,400,589.83
249-9806-5192 - Secondary District Wide - Portable Classrooms	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
249-9821-5192 - Secondary District Wide - Roofing Replacement	\$0.00	(\$390.92)	(\$11,950.00)	\$390.92	(\$12,340.92)
249-9851-5192 - Secondary District Wide - Site Improvements	\$0.00	(\$9,444.40)	\$0.00	\$9,444.40	(\$9,444.40)
249-9861-5192 - Secondary District Wide - Management	\$6,579.04	\$15,001.64	(\$25,776.64)	(\$8,422.60)	(\$10,775.00)
249-9900-5189 - Secondary District Wide - Tech. Infrastructure	\$268,414.82	\$500,956.07	(\$821,119.27)	(\$232,541.25)	(\$320,163.20)
249-9902-5189 - Secondary District Wide - Phone Intercom System	\$0.00	\$175,714.74	(\$192,671.52)	(\$175,714.74)	(\$16,956.78)
249-9907-5189 - Secondary District Wide - Technology Other	\$418,970.63	\$1,088,755.95	(\$3,153,968.68)	(\$669,785.32)	(\$2,065,212.73)
249-9977-5192 - Secondary District Wide - Master Plan - Infrastruc	\$0.00	(\$7,160.00)	\$0.00	\$7,160.00	(\$7,160.00)
250-9500-5192 - Montgomery High - Athletic Fields	\$20,100.00	\$3,000.00	\$0.00	\$17,100.00	\$3,000.00
250-9502-5192 - Montgomery High - Track Repairs	\$1,976,591.47	\$1,976,591.47	\$0.00	\$0.00	\$1,976,591.47
250-9654-5192 - Montgomery High - Restroom Reconditioning	\$0.00	(\$18,531.29)	\$0.00	\$18,531.29	(\$18,531.29)
250-9800-5192 - Montgomery High - Permanent Bldgs New	\$10,500.00	\$1,150,741.00	(\$369,577.80)	(\$1,140,241.00)	\$781,163.20
250-9821-5192 - Montgomery High - Roofing Replacement	\$162,750.00	\$162,750.00	(\$162,750.00)	\$0.00	\$0.00
250-9851-5192 - Montgomery High - Site Improvements	\$243,389.00	\$373,269.00	(\$352,268.25)	(\$129,880.00)	\$21,000.75
251-9500-5192 - Piner High - Athletic Fields	\$19,700.00	\$3,000.00	\$0.00	\$16,700.00	\$3,000.00
251-9502-5192 - Piner High - Track Repairs	\$1,882,011.48	\$1,877,015.40	\$0.00	\$4,996.08	\$1,877,015.40
251-9506-5192 - Piner High - Athletic Field Lighting	\$3,760.00	\$30,130.00	(\$1,619,875.65)	(\$26,370.00)	(\$1,589,745.65)
251-9540-5192 - Piner High - Asbestos/Hazardous Materials	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
251-9566-5192 - Piner High - School Signage	\$9,317.85	\$0.00	\$0.00	\$9,317.85	\$0.00
251-9654-5192 - Piner High - Restroom Reconditioning	\$0.00	(\$18,531.29)	\$0.00	\$18,531.29	(\$18,531.29)
251-9821-5192 - Piner High - Roofing Replacement	\$0.00	(\$25,757.00)	(\$264,946.25)	\$25,757.00	(\$290,703.25)
251-9851-5192 - Piner High - Site Improvements	\$38,727.91	\$75,587.94	(\$325,462.93)	(\$36,860.03)	(\$249,874.99)
252-9500-5192 - Santa Rosa High - Athletic Fields	\$18,821.00	\$3,000.00	\$0.00	\$15,821.00	\$3,000.00

2018 Program Summary - Measure I January 1, 2018 - December 31, 2018

PROJECT	BUD TOTAL	ENCUMBERED	DISBURSEMENT	BUD REMAIN.	ENC BALANCE
252-9502-5192 - Santa Rosa High - Track Repairs	\$1,921,066.10	\$0.00	\$0.00	\$1,921,066.10	\$0.00
252-9654-5192 - Santa Rosa High - Restroom Reconditioning	\$0.00	(\$29,120.61)	\$0.00	\$29,120.61	(\$29,120.61)
252-9821-5192 - Santa Rosa High - Roofing Replacement	\$84,750.00	\$5,425,707.90	(\$3,789,343.72)	(\$5,340,957.90)	\$1,636,364.18
253-9500-5192 - Elsie Allen High - Athletic Fields	\$19,700.00	\$3,000.00	\$0.00	\$16,700.00	\$3,000.00
253-9502-5192 - Elsie Allen High - Track Repairs	\$1,931,061.60	\$0.00	\$0.00	\$1,931,061.60	\$0.00
253-9566-5192 - Elsie Allen High - School Signage	\$9,317.85	\$0.00	\$0.00	\$9,317.85	\$0.00
253-9654-5192 - Elsie Allen High - Restroom Reconditioning	\$0.00	(\$10,589.31)	\$0.00	\$10,589.31	(\$10,589.31)
253-9821-5192 - Elsie Allen High - Roofing Replacement	\$0.00	\$9,582,395.66	(\$5,995,660.91)	(\$9,582,395.66)	\$3,586,734.75
254-9500-5192 - Maria Carrillo High - Athletic Fields	\$4,627.24	\$33,189.60	(\$25,465.60)	(\$28,562.36)	\$7,724.00
254-9502-5192 - Maria Carrillo High - Track Repairs	\$0.00	(\$968,172.77)	(\$2,750,377.56)	\$968,172.77	(\$3,718,550.33)
254-9536-5192 - Maria Carrillo High - Site Improvements 1	\$135,000.00	\$135,000.00	\$0.00	\$0.00	\$135,000.00
254-9650-5192 - Maria Carrillo High - Traffic Flow	\$9,238.71	\$5,788.26	(\$5,788.26)	\$3,450.45	\$0.00
254-9654-5192 - Maria Carrillo High - Restroom Reconditioning	\$0.00	(\$7,941.99)	\$0.00	\$7,941.99	(\$7,941.99)
254-9800-5192 - Maria Carrillo High - Permanent Bldgs New	\$0.00	\$15,378.00	(\$15,378.00)	(\$15,378.00)	\$0.00
254-9821-5192 - Maria Carrillo High - Roofing Replacement	\$189,307.65	\$6,651,920.31	(\$4,297,560.99)	(\$6,462,612.66)	\$2,354,359.32
254-9851-5192 - Maria Carrillo High - Site Improvements	\$5,141.76	\$26,641.76	(\$22,464.56)	(\$21,500.00)	\$4,177.20
260-9654-5192 - Ridgway Continuation High - Restroom Reconditionin	\$0.00	(\$5,294.65)	\$0.00	\$5,294.65	(\$5,294.65)
291-9305-9795 - Secondary For Director Dp - Operations Services	\$0.00	\$34,940.21	(\$34,940.21)	(\$34,940.21)	\$0.00
292-9305-9795 - Secondary For Asst Sup Busines - Operations Servic	\$31,861.24	\$40,219.67	(\$40,219.67)	(\$8,358.43)	\$0.00
Grand Total	\$12,414,214.51	\$40,464,103.17	(\$32,311,858.29)	(\$28,049,888.66)	\$8,152,244.88

Overall Program Summary (all years through 2018)

PROJECT	BUD TOTAL	ENCUMBERED	DISBURSEMENT	BUD REMAIN.	ENC BALANCE
000-0000-0000 - District Wide	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
200-0000-0000 - Secondary Schools	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
200-9650-5192 - Secondary Schools - Other Fees	\$64,761.00	\$64,761.00	(\$64,761.00)	\$0.00	\$0.00
230-9650-5192 - Cook Middle - Other Fees	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
230-9806-5192 - Cook Middle - Portable Classrooms	\$858,632.15	\$858,632.15	(\$857,598.13)	\$0.00	\$1,034.02
230-9810-5192 - Cook Middle - Portable Restroom	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
230-9817-5192 - Cook Middle - HVAC Replacement	\$10,490.00	\$10,490.00	(\$10,490.00)	\$0.00	\$0.00
230-9851-5192 - Cook Middle - Site Improvements	\$22,886.16	\$22,886.16	(\$22,886.16)	\$0.00	\$0.00
230-9875-5192 - Cook Middle - Modernization	\$2,631.88	\$2,631.88	(\$2,631.88)	\$0.00	\$0.00
230-9876-5192 - Cook Middle - Modernization 2	\$20,223.72	\$20,223.72	(\$20,223.72)	\$0.00	\$0.00
231-9540-5192 - Slater Middle - Asbestos/Hazardous Materials	\$57,984.00	\$55,348.00	(\$55,348.00)	\$2,636.00	\$0.00
231-9566-5192 - Slater Middle - School Signage	\$27,976.04	\$27,976.04	(\$27,976.04)	\$0.00	\$0.00
231-9650-5192 - Slater Middle - Other Fees	\$78,750.00	\$78,750.00	(\$78,750.00)	\$0.00	\$0.00
231-9821-5192 - Slater Middle - Roofing Replacement	\$733,812.00	\$733,812.00	(\$722,387.00)	\$0.00	\$11,425.00
232-9532-5192 - Comstock Middle - Security	\$13,891.00	\$13,891.00	(\$13,891.00)	\$0.00	\$0.00
232-9540-5192 - Comstock Middle - Asbestos/Haz. Mat.	\$1,038.00	\$1,038.00	(\$1,038.00)	\$0.00	\$0.00
232-9806-5192 - Comstock Middle - Portable Classrooms	\$86,900.00	\$86,900.00	(\$6,083.00)	\$0.00	\$80,817.00
232-9821-5192 - Comstock Middle - Roofing Replacement	\$5,102,813.90	\$6,197,666.76	(\$4,389,791.20)	(\$1,094,852.86)	\$1,807,875.56
232-9851-5192 - Comstock Middle - Site Improvements	\$12,853.16	\$12,853.16	(\$12,853.16)	\$0.00	\$0.00
232-9876-5192 - Comstock Middle - Modernization 2	\$20,223.73	\$20,223.73	(\$20,223.73)	\$0.00	\$0.00
233-9531-5192 - Rincon Valley Middle - Site Safety	\$43,841.00	\$43,841.00	(\$43,841.00)	\$0.00	\$0.00
233-9806-5192 - Rincon Valley Middle - Portable Classrooms	\$2,249.35	\$2,249.35	(\$2,249.35)	\$0.00	\$0.00
233-9875-5192 - Rincon Valley Middle - Modernization	\$669.00	\$669.00	(\$669.00)	\$0.00	\$0.00
234-9851-5192 - Santa Rosa Middle - Site Improvements	\$61,050.00	\$61,050.00	\$0.00	\$0.00	\$61,050.00
243-9816-5189 - Lewis / Alternative Ed - Hvac Systems	\$22,987.00	\$22,987.00	\$0.00	\$0.00	\$22,987.00
249-0000-5192 - Secondary District Wide - Undistributed	\$12,084.50	\$12,084.50	(\$12,084.50)	\$0.00	\$0.00
249-9400-5192 - Secondary District Wide - Bond Election Costs	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
249-9402-5192 - Secondary District Wide - Bond Election 2014	(\$50,407.42)	(\$50,407.42)	\$50,407.42	\$0.00	\$0.00
249-9403-5192 - Secondary District Wide - Security	\$46,000.00	\$46,000.00	(\$46,000.00)	\$0.00	\$0.00
249-9500-5192 - Secondary District Wide - Athletic Fields	\$443.21	\$0.00	\$0.00	\$443.21	\$0.00
249-9531-5192 - Secondary District Wide - Site Safety	\$66,240.64	\$66,240.64	(\$66,240.64)	\$0.00	\$0.00
249-9650-5192 - Secondary District Wide - Other Fees	\$6,178,046.95	\$6,141,840.00	(\$3,716,555.19)	\$36,206.95	\$2,425,284.81
249-9806-5192 - Secondary District Wide - Portable Classrooms	\$410,935.08	\$410,935.08	(\$405,095.08)	\$0.00	\$5,840.00
249-9816-5192 - Secondary District Wide - Hvac Systems	\$25,359.90	\$25,359.90	(\$25,359.90)	\$0.00	\$0.00
249-9817-5192 - Secondary District Wide - Hvac Replacement	\$7,953.40	\$7,953.40	(\$7,953.40)	\$0.00	\$0.00
249-9821-5192 - Secondary District Wide - Roofing Replacement	\$178,859.08	\$178,859.08	(\$178,859.08)	\$0.00	\$0.00
249-9851-5192 - Secondary District Wide - Site Improvements	\$8,988.50	\$8,988.50	(\$8,988.50)	\$0.00	\$0.00
249-9852-5192 - Secondary District Wide - Site Improvement 2	\$304,131.76	\$304,131.76	(\$304,131.76)	\$0.00	\$0.00
249-9861-5192 - Secondary District Wide - Management	\$82,666.24	\$74,266.24	(\$74,047.24)	\$8,400.00	\$219.00
249-9900-5189 - Secondary District Wide - Tech. Infrastructure	\$7,289,162.63	\$7,252,853.88	(\$7,089,916.79)	\$36,308.75	\$162,937.09
249-9902-5189 - Secondary District Wide - Phone Intercom System	\$2,725,751.53	\$2,725,751.53	(\$2,703,031.56)	\$0.00	\$22,719.97

Overall Program Summary (all years through 2018)

PROJECT	BUD TOTAL	ENCUMBERED	DISBURSEMENT	BUD REMAIN.	ENC BALANCE
249-9907-5189 - Secondary District Wide - Technology Other	\$10,574,184.95	\$10,574,184.95	(\$9,966,774.13)	\$0.00	\$607,410.82
249-9977-5192 - Secondary District Wide - Master Plan - Infrastruc	\$1,704,260.52	\$1,704,260.52	(\$1,704,260.52)	\$0.00	\$0.00
250-9500-5192 - Montgomery High - Athletic Fields	\$20,100.00	\$3,000.00	\$0.00	\$17,100.00	\$3,000.00
250-9502-5192 - Montgomery High - Track Repairs	\$1,976,591.47	\$1,976,591.47	\$0.00	\$0.00	\$1,976,591.47
250-9654-5192 - Montgomery High - Restroom Reconditioning	\$16,709.62	\$16,709.62	(\$16,709.62)	\$0.00	\$0.00
250-9800-5192 - Montgomery High - Permanent Bldgs New	\$1,150,741.00	\$1,150,741.00	(\$369,577.80)	\$0.00	\$781,163.20
250-9821-5192 - Montgomery High - Roofing Replacement	\$162,750.00	\$162,750.00	(\$162,750.00)	\$0.00	\$0.00
250-9851-5192 - Montgomery High - Site Improvements	\$613,319.00	\$373,269.00	(\$352,268.25)	\$240,050.00	\$21,000.75
251-9500-5192 - Piner High - Athletic Fields	\$19,700.00	\$3,000.00	\$0.00	\$16,700.00	\$3,000.00
251-9502-5192 - Piner High - Track Repairs	\$1,882,011.48	\$1,877,015.40	\$0.00	\$4,996.08	\$1,877,015.40
251-9506-5192 - Piner High - Athletic Field Lighting	\$1,963,555.98	\$1,963,555.98	(\$1,863,828.14)	\$0.00	\$99,727.84
251-9540-5192 - Piner High - Asbestos/Hazardous Materials	\$5,430.00	\$5,430.00	(\$3,687.00)	\$0.00	\$1,743.00
251-9566-5192 - Piner High - School Signage	\$9,317.85	\$0.00	\$0.00	\$9,317.85	\$0.00
251-9654-5192 - Piner High - Restroom Reconditioning	\$16,709.62	\$16,709.62	(\$16,709.62)	\$0.00	\$0.00
251-9821-5192 - Piner High - Roofing Replacement	\$3,996,264.00	\$3,996,264.00	(\$3,950,817.99)	\$0.00	\$45,446.01
251-9851-5192 - Piner High - Site Improvements	\$388,749.87	\$388,749.87	(\$368,963.86)	\$0.00	\$19,786.01
251-9861-5192 - Piner High - Management	\$3,000.00	\$3,000.00	(\$3,000.00)	\$0.00	\$0.00
251-9900-5192 - Piner High - Technology Infrastructure	\$24,200.00	\$24,200.00	(\$24,200.00)	\$0.00	\$0.00
252-9500-5192 - Santa Rosa High - Athletic Fields	\$18,821.00	\$3,000.00	\$0.00	\$15,821.00	\$3,000.00
252-9502-5192 - Santa Rosa High - Track Repairs	\$1,921,066.10	\$0.00	\$0.00	\$1,921,066.10	\$0.00
252-9654-5192 - Santa Rosa High - Restroom Reconditioning	\$26,257.97	\$26,257.97	(\$26,257.97)	\$0.00	\$0.00
252-9821-5192 - Santa Rosa High - Roofing Replacement	\$5,425,707.90	\$5,425,707.90	(\$3,789,343.72)	\$0.00	\$1,636,364.18
252-9851-5192 - Santa Rosa High - Site Improvements	\$14,552.00	\$14,552.00	(\$14,552.00)	\$0.00	\$0.00
253-9500-5192 - Elsie Allen High - Athletic Fields	\$19,700.00	\$3,000.00	\$0.00	\$16,700.00	\$3,000.00
253-9502-5192 - Elsie Allen High - Track Repairs	\$1,931,061.60	\$0.00	\$0.00	\$1,931,061.60	\$0.00
253-9566-5192 - Elsie Allen High - School Signage	\$9,317.85	\$0.00	\$0.00	\$9,317.85	\$0.00
253-9654-5192 - Elsie Allen High - Restroom Reconditioning	\$9,548.35	\$9,548.35	(\$9,548.35)	\$0.00	\$0.00
253-9817-5192 - Elsie Allen High - HVAC Replacement	\$8,955.00	\$8,955.00	(\$8,955.00)	\$0.00	\$0.00
253-9821-5192 - Elsie Allen High - Roofing Replacement	\$7,791,572.55	\$9,582,395.66	(\$5,995,660.91)	(\$1,790,823.11)	\$3,586,734.75
253-9851-5192 - Elsie Allen High - Site Improvements	\$75,668.77	\$75,668.77	(\$75,668.77)	\$0.00	\$0.00
254-9500-5192 - Maria Carrillo High - Athletic Fields	\$38,889.60	\$38,889.60	(\$31,165.60)	\$0.00	\$7,724.00
254-9502-5192 - Maria Carrillo High - Track Repairs	\$5,047,519.15	\$5,047,519.15	(\$4,608,423.29)	\$0.00	\$439,095.86
254-9536-5192 - Maria Carrillo High - Site Improvements 1	\$135,000.00	\$135,000.00	\$0.00	\$0.00	\$135,000.00
254-9650-5192 - Maria Carrillo High - Traffic Flow	\$21,376.97	\$12,138.26	(\$12,138.26)	\$9,238.71	\$0.00
254-9654-5192 - Maria Carrillo High - Restroom Reconditioning	\$7,161.27	\$7,161.27	(\$7,161.27)	\$0.00	\$0.00
254-9800-5192 - Maria Carrillo High - Permanent Bldgs New	\$15,378.00	\$15,378.00	(\$15,378.00)	\$0.00	\$0.00
254-9821-5192 - Maria Carrillo High - Roofing Replacement	\$5,498,923.55	\$6,651,920.31	(\$4,297,560.99)	(\$1,152,996.76)	\$2,354,359.32
254-9851-5192 - Maria Carrillo High - Site Improvements	\$70,258.82	\$70,258.82	(\$57,766.62)	\$0.00	\$12,492.20
260-9654-5192 - Ridgway Continuation High - Restroom Reconditionin	\$4,774.18	\$4,774.18	(\$4,774.18)	\$0.00	\$0.00
260-9806-5192 - Ridgway Continuation High - Portable Classrooms	\$10,195.62	\$10,195.62	(\$10,195.62)	\$0.00	\$0.00
260-9808-5192 - Ridgway Continuation High - Portable Classroom	\$90,921.52	\$90,921.52	(\$90,921.52)	\$0.00	\$0.00

Overall Program Summary (all years through 2018)

PROJECT	BUD TOTAL	ENCUMBERED	DISBURSEMENT	BUD REMAIN.	ENC BALANCE
260-9851-5192 - Ridgway Continuation High - Site Improvements	\$23,000.00	\$23,000.00	(\$23,000.00)	\$0.00	\$0.00
260-9854-5192 - Ridgway Continuation High - Site Improvements 4	\$26,858.92	\$26,858.92	(\$26,858.92)	\$0.00	\$0.00
260-9875-5192 - Ridgway Continuation High - Modernization	\$1,094.88	\$1,094.88	(\$1,094.88)	\$0.00	\$0.00
291-9305-9795 - Secondary For Director Dp - Operations Services	\$251,024.85	\$251,024.85	(\$251,024.85)	\$0.00	\$0.00
292-9305-9795 - Secondary For Asst Sup Busines - Operations Servic	\$131,535.87	\$116,363.37	(\$116,363.37)	\$15,172.50	\$0.00
389-9907-5189 - Technology District Wide - Technology Other	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00
389-9907-5192 - Technology District Wide - Technology Other	\$1,216.71	\$1,216.71	(\$1,216.71)	\$0.00	\$0.00
392-9535-5192 - Business - Site Improvements	\$877.12	\$877.12	(\$877.12)	\$0.00	\$0.00
Grand Total	\$77,688,710.57	\$77,436,846.70	(\$59,221,002.44)	\$251,863.87	\$18,215,844.26

Fiscal and Performance Audit

The COC has reviewed

1. The Audit Report dated January 31, 2018 for year ended June 30, 2017 and prepared by Chavan & Associates, LLP, Certified Public Accountants. This report included the following:

- Independent Auditor's Report
- Program Statements
- Schedule of Findings and Recommendations
- Other Independent Auditor's Reports
- The Audit Report can be found at <http://www.srcschools.org>

Schedule of Findings and Recommendations from the audit:

- The audit tests resulted in no findings and recommendations


Schedule of Prior Year Findings and Recommendations from the audit:

- There were no prior year findings and recommendations to be reported

2. District prepared financial reports dated January 18, 2018, April 19, 2018, Aug. 23, 2018, and December 19, 2018. These reports can be found at <http://www.srcschools.org>.

Photos

Maria Carrillo High School track and turf installation:

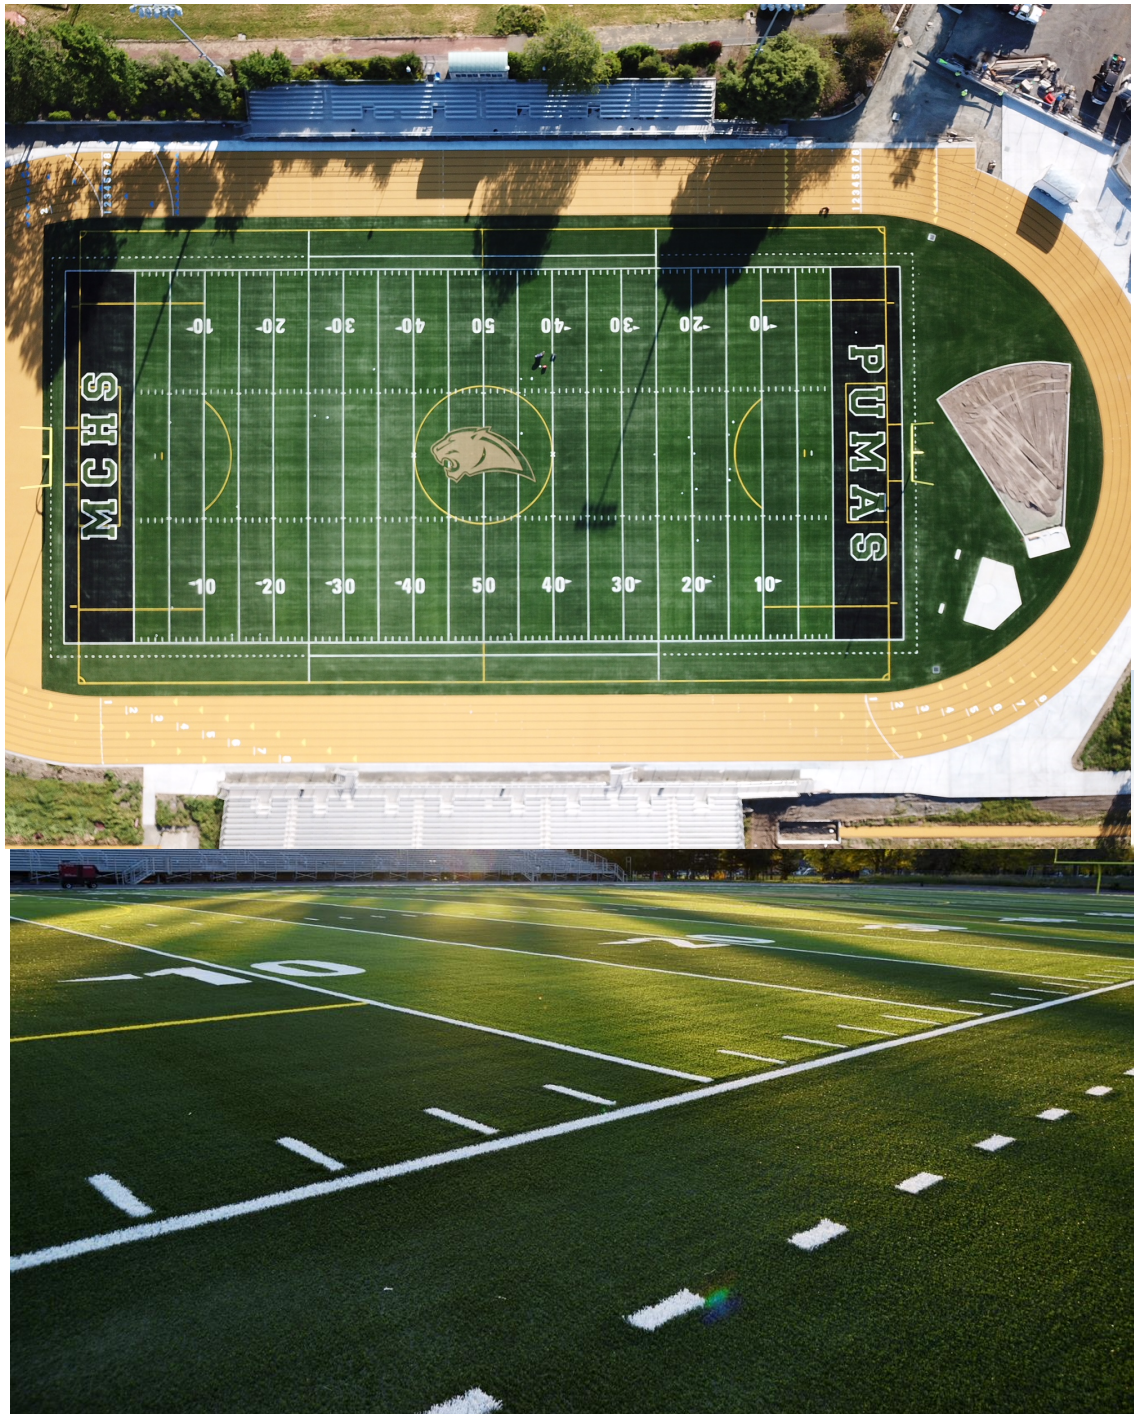

Piner High School Stadium Lights:



Piner High School New Retaining Wall



Elsie Allen High School Roofing and HVAC:




Santa Rosa High Phase I Roofing and HVAC:



Technology Projects

New network equipment installed at all sites

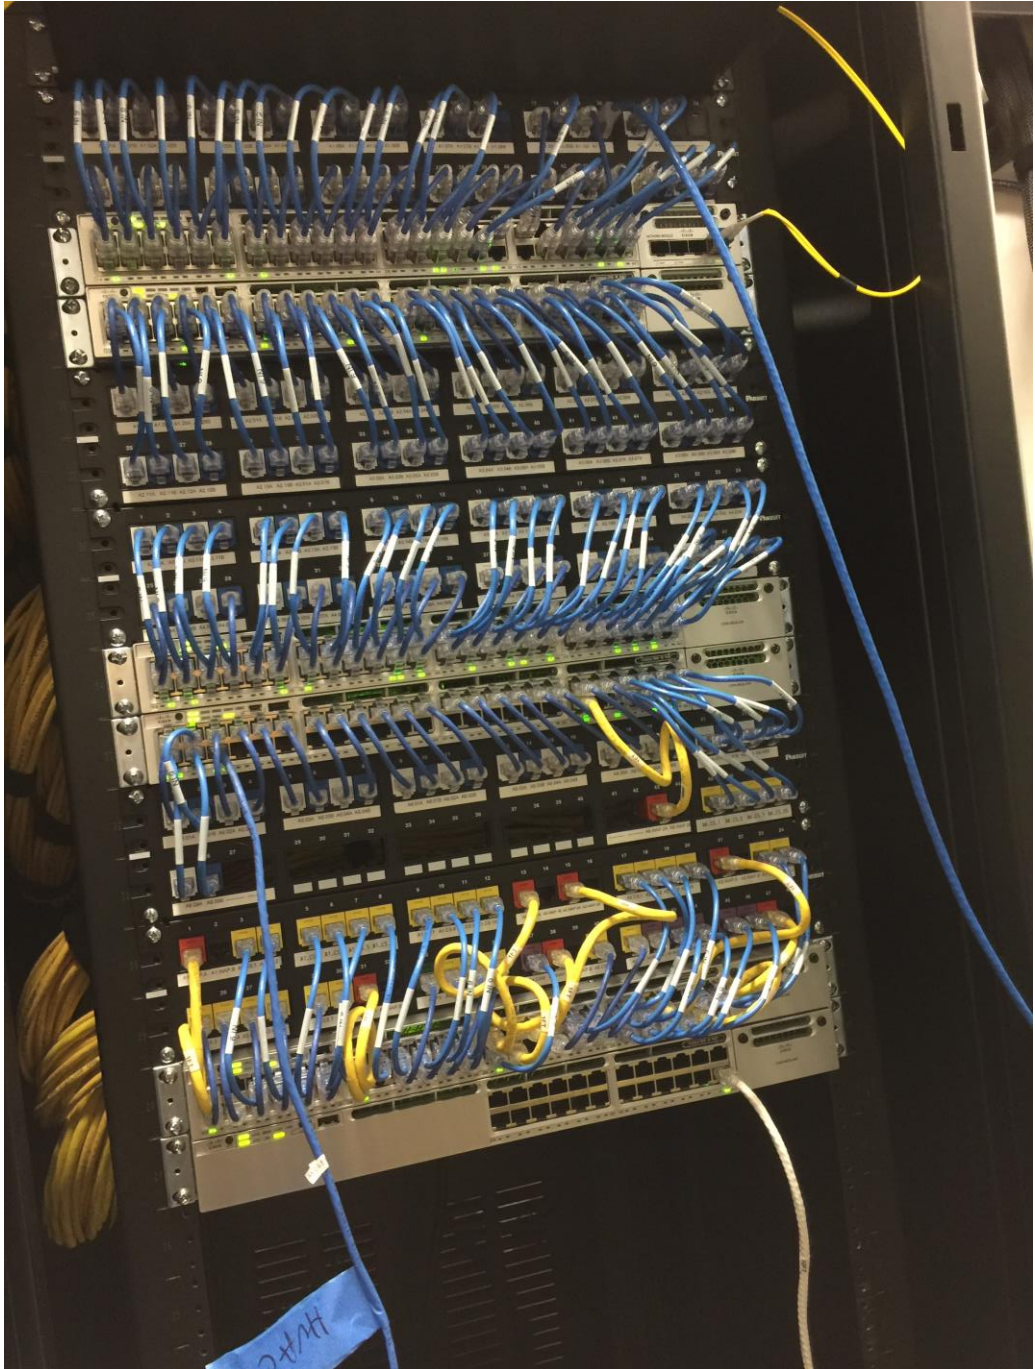



New phone system installed at all sites



New bell/clock system installed at all sites



Presentation of the 2017 Annual Report to the Santa Rosa City School Board:



Committee Members

Committee Members 2017-2020			
Position	Name	Term Expires	
Chair (Business Organization)	Mike Behler	2020	3 year term
Vice Chair (Senior Citizen's Organization)	Carolina Spence	2020	3 year term
Member (At Large)	Mindy Breslin	2021	3 year term
Member (At Large)	Kristin Hendricks	2020	3 year term
Member (At Large)	Chris Nelle	2018	3 year term
Member (Taxpayer's Organization)	Kirk Veale	2018	3 year term
Member (Parent or Guardian)	Vacant		
Member (Parent or Guardian, active PTO)	Vacant		

Contact Information

Measure I Bond

Rick Edson, Deputy Superintendent



Santa Rosa City Schools

211 Ridgway Avenue Santa Rosa, CA 95401

Tel (707) 890-3800 x80201

<http://www.srcschools.org>
